



Odisha Integrated Irrigation Project for Climate Resilient Agriculture (P163533)

SOUTH ASIA | India | IBRD/IDA | Investment Project Financing (IPF) | FY 2020 | Seq No: 16 | Archived on 25-Sep-2026 | ISR09186

Implementing Agencies: Agricultural Promotion and Investment Corporation of Odisha Limited, Odisha Community Tank Development and Management Society, Department of Water Resources

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Approval package on 30-Sep-2019)
The Project Development Objective is to intensify and diversify agricultural production, and enhance climate resilience in selected districts of Odisha.

Has the Development Objective been changed since Board Approval of the Project Objective?
No

2. COMPONENTS

Name
Climate-Smart Intensification and Diversification of Production:(Cost \$77.99)
Improving Access to Irrigation and Water Productivity:(Cost \$75.74)
Institutional Capacity Strengthening:(Cost \$9.89)
Project Management:(Cost \$6.84)
Contingent Emergency Response:(Cost \$0)

3. OVERALL RATINGS

Name	Previous	Current
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	● Substantial	● Substantial



4. KEY ISSUES & STATUS

4.1 Implementation Status and Key Decisions

This is an interim ISR being filed to update selected Agriconnect-related indicators.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval Approval Package - 30 Sep 2019	Last Approved Rating ISR Seq. 015 - 13 Apr 2026	Proposed Rating
Political and Governance	● Low	● Low	● Low
Macroeconomic	● Low	● Low	● Low
Sector Strategies and Policies	● Moderate	● Moderate	● Moderate
Technical Design of Project or Program	● Moderate	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	● Moderate	● Moderate	● Moderate
Fiduciary	● Moderate	● Moderate	● Moderate
Environment and Social	● Substantial	● Moderate	● Moderate
Stakeholders	● Moderate	● Moderate	● Moderate
Overall	● Substantial	● Substantial	● Substantial



6. RESULTS

6.1 PDO Indicators by PDO Outcomes

To intensify and diversify agricultural production in selected districts of Odisha								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Increase in productivity of selected agricultural commodities supported by the project (Percentage)	0.00	Aug/2019	67	Feb/2026	67	Feb/2026	50.00	Jun/2027
	Comments on achieving targets		The indicator measures percentage changes in crop or fish yields. It measures yield increase from target beneficiaries who are adopting practices promoted by the project. Beyond Paddy, Green Gram, Brinjal, Groundnuts and Marigold, the project will also capture productivity changes for Black Gram, Sunflower, Tomato, Cabbage, Cauliflower, Bitter Gourd or any other crops that receive project financing.					
Increase in productivity of selected agricultural commodities supported by the project produced by female beneficiaries (Percentage)	0.00	Aug/2020	158	Feb/2026	158	Feb/2026	50	Jun/2027
	Comments on achieving targets		Household survey yet to be conducted and reported.					
Increase in productivity of water use at tank level (Percentage)	0.00	Aug/2019	28	Feb/2026	28	Feb/2026	25	Jun/2027
	Comments on achieving targets		This indicator measures crop yield per unit input of water. Data yet to be collected and reported.					
Share of non-rice commodities in total production in project areas (Percentage)	33.00	Aug/2020	57	Feb/2026	57	Feb/2026	38.00	Jun/2027
	Comments on achieving targets		This indicator measures the proportion of total cultivated area that is devoted to other crops than rice. It is a measure of diversification away from rice.					



Share of non-rice products in total production in project areas produced by female beneficiaries (Percentage)	33.00	Aug/2020	57	Feb/2026	57	Feb/2026	38.00	Jun/2027
Share of target beneficiaries with rating "Satisfied" or above on process and impact of project interventions (Percentage)	0.00	Aug/2020	94	Feb/2026	94	Feb/2026	80.00	Jun/2027
	Comments on achieving targets		The indicator measures the share of beneficiaries who are satisfied with the relevance, timeliness, and effectiveness of the services received from the project.					
Share of target female beneficiaries with rating "Satisfied" or above on process and impact of project interventions (Percentage)	0.00	Aug/2020	92	Feb/2026	92	Feb/2026	80	Jun/2027
To enhance climate resilience in selected districts of Odisha								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Farmers adopting improved agricultural technology (Number)	0.00	Aug/2020	86,048	Feb/2026	163,068	Sep/2026	100,000	Jun/2027
	Comments on achieving targets		This indicator measures the number of farmers (of agricultural products) who have adopted an improved agricultural technology promoted by operations supported by the World Bank. NB: "Agriculture" or "Agricultural" includes: crops, livestock, capture fisheries, aquaculture, agroforestry, timber and non-timber forest products. Adoption refers to a change of practice or change in use of a technology that was introduced or promoted by the project. Technology includes a change in practices compared to currently used practices or					



			technologies (seed preparation, planting time, feeding schedule, feeding ingredients, postharvest storage/ processing, etc.). If the project introduces or promotes a technology package in which the benefit depends on the application of the entire package (e.g., a combination of inputs such as a new variety and advice on agronomic practices such as soil preparation, changes in seeding time, fertilizer schedule, plant protection, etc.), this counts as one technology. Farmers are people engaged in farming of agricultural products or members of an agriculture related business (disaggregated by men and women) targeted by the project.					
Farmers adopting improved agricultural technology - Female (Number)	0.00		23,233		23,233		40,000	
	Comments on achieving targets		Gender disaggregated data is being verified, this value is roughly 42% of total farmers, consistent with previous period trend of proportion female farmers					

6.2 Intermediate Results Indicators by Components

Climate-Smart Intensification and Diversification of Production								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Share of beneficiary farmers' produce that is marketed facilitated by the project (Percentage)	10.00	Aug/2020	85.80	Aug/2025	85.80	Aug/2025	30.00	Jun/2027
	Comments on achieving targets		This refers to the proportion of total farm output which beneficiary farmers are able to market facilitated by the project controlled for increased production.					
Share of female beneficiary farmers' produce that is marketed facilitated by the project (Percentage)	10.00	Aug/2020	86.50	Aug/2025	86.50	Aug/2025	30.00	Jun/2027
	15.00	Aug/2020	37	Aug/2025	37	Aug/2025	30.00	Jun/2027



Increase in share of project beneficiary farmers with access to resilient seeds (Percentage)	Comments on achieving targets		This refers to the number of project beneficiaries who report increased access to resilient varieties directly promoted by the project.					
			The original indicator is no longer relevant following the changes made to the fisheries activities during the restructuring. A new indicator ' "Percentage increase in aquaculture production by farmers, following adoption of climate resilient technologies of promoted by the project", will be the new indicator. The end target will be 20%. The change will be made formally.					
Increase in share of female beneficiary farmers with access to resilient seeds (Percentage)	15.00	Aug/2020	37	Aug/2025	37	Aug/2025	30.00	Jun/2027
Increase in aquaculture production by farmers, following adoption of climate resilient technologies of promoted by the project (Percentage)	0.71	Mar/2024	195	Aug/2025	195	Aug/2025	20.00	Jun/2027
Improving Access to Irrigation and Water Productivity								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Area provided with new/improved irrigation or drainage services (Hectare (Ha))	0.00	Aug/2020	26,383	Feb/2026	30,131	Sep/2026	72,805.00	Jun/2027
	Comments on achieving targets		This indicator measures the total area of land provided with irrigation and drainage services under the project, including in (i) the area provided with new irrigation and drainage services, and (ii) the area provided with improved irrigation and drainage services, expressed in hectare (ha).					
	0.00	Aug/2020	100	Feb/2026	100	Feb/2026	50.00	Aug/2025




Share of project-supported schemes meeting at least 50% of scheme performance targets (Percentage)	Comments on achieving targets		Data is being collected					
Increase in area under crops that are less water demanding. (Percentage)	0.00	Aug/2019	50.64	Feb/2026	50.64	Feb/2026	30.00	Aug/2025
	Comments on achieving targets		This indicator measures the area planted with crops that are scientifically known to consume less water than the conventional rice. This could include areas planted to less water demanding rice varieties. It measures annual increases including both Kharif and Rab seasons					
Proportion of project supported PPs with women representation (Percentage)	0.00	May/2019	92.90	Feb/2026	92.90	Feb/2026	35.00	Aug/2025
	Comments on achieving targets		This indicator measures the number of PPs with women in the executive committee havng voice and decision making power					
Institutional Capacity Strengthening								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Government staff trained through project support (Number)	0.00	Aug/2020	789	Feb/2026	789	Feb/2026	200.00	Aug/2025
	Comments on achieving targets		This refers to number of GoO staff whose capacity is strengthened through project support. This will measure all types of training supported by the project.					
Percentage of government staff trained through project support – Female (Percentage)	0.00	Aug/2020	36	Feb/2026	36	Feb/2026	50.00	Aug/2025



7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

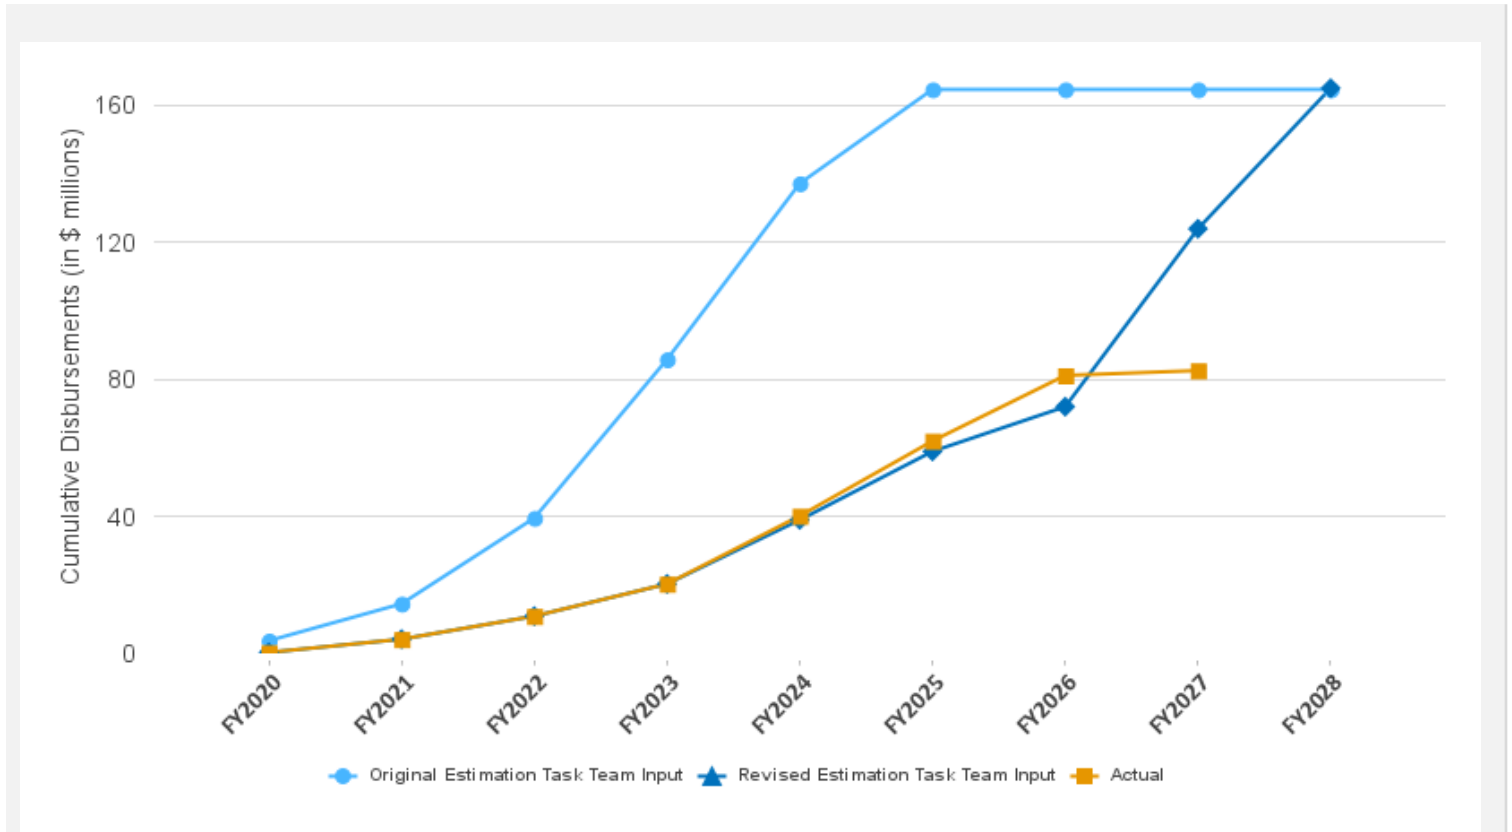

7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	Historical Disbursed	% Disbursed
IBRD-90110	Effective	165.00	119.32	45.68	82.98	36.34	82.98	69.54%

7.3 Key Dates (by loan)

Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
IBRD-90110	Effective	30-Sep-2019	24-Oct-2019	16-Dec-2019	31-Dec-2025	30-Jun-2027

8. KEY DATES



Key Events	Planned	Actual
Approval	30-Sep-2019	30-Sep-2019
Effectiveness	16-Dec-2019	16-Dec-2019
Mid-Term Review No. 01	12-Dec-2022	21-Dec-2022
Operation Closing/Cancellation	30-Jun-2027	

9. RESTRUCTURING HISTORY

Restructuring Level 2 Approved on 27-Oct-2021

Restructuring Level 2 Approved on 07-Jun-2023

Restructuring Level 2 Approved on 16-Feb-2021

Restructuring Level 2 Approved on 12-Sep-2024

Restructuring Level 2 Approved on 05-Dec-2025

10. ASSOCIATED OPERATION(S)

There are no associated operations
